

SportSmart MVP Sprint Plan

Eight weeks from where we are to live commercial operations.

15 July 2026

The plan in 60 seconds

Read this page. Skip the rest if you trust the team.

We're 57% of the way to MVP. The platform works end-to-end in staging today — customers can browse, sellers can list, franchises can sell at POS, admins can run the back office, GST invoices generate correctly. What's left is closing 3 ship-blockers, hardening for real load, and operationalising what we've built (alerts, dashboards, runbooks, training). Four 2-week sprints get us there with a 2-day buffer before launch on **Wednesday 15 July**.

15

JUL · LAUNCH

4

SPRINTS

4.0

FTE

GREEN

CONFIDENCE

What I need from you

1. **Endorse the 15 July date.** If anything in the timeline below looks shaky, say so this week, not in week six.
2. **Confirm team composition:** 1 Eng Lead + 1 Backend + 1 Frontend + 0.5 QA + 0.25 DevOps. Same team for all four sprints.
3. **Accept the post-MVP defer list** (page 4). These items don't make MVP; they're in the next quarter's plan.
4. **Co-sign Go/No-Go on 12 July.** Default decision is No-Go unless every CRITICAL exit-criterion is met.

The three things I'm watching

RISK	RAG	WHAT I'M DOING ABOUT IT
Concurrent-order race could cause oversell on Day 1	AMBER	Sprint 2 fixes the race. Sprint 4 load test proves it under realistic concurrency.
Stuck refunds pile up because the recovery cron doesn't exist yet	AMBER	Sprint 1 ships the cron. Finance monitors the queue daily from day one.
Payment gateway outage on launch day	GREEN	COD stays available. Status page wired. Customer comms drafted.

Bottom line: We launch on 15 July with high confidence if Sprints 1 and 2 deliver on plan. If Sprint 1 slips, we re-plan in the 1 June review. If Sprint 2 slips, we'll have an honest conversation about a 2-week date push before we get to Sprint 4. No surprises in the last week.

1. Where we are today

The platform has matured through 28 phases of engineering. Today, against MVP scope, the picture looks like this:

CAPABILITY	STATUS	WHAT'S LEFT
Customer browse, cart, checkout, payment	75%	Cart race condition; one frontend hang on API errors
Seller onboarding, GSTIN/PAN, product listing	95%	Server-side logout; admin can't edit seller GSTIN yet (defer)
Franchise POS, procurement, settlements	80%	POS cross-state tax split; procurement per-line tax (defer)
Order placement, allocation, fulfilment	80%	Inventory write path needs end-to-end verification
Payments, refunds (online + COD), wallet	70%	COD UPI auto-refund; stuck-saga recovery cron; settlement drift
GST: invoices, e-invoice, e-way bill, GSTR reports	95%	External CA sign-off on POS bills
Admin tools: approvals, finance, tax dashboard	90%	Some silent-error frontend bugs
Identity: 5 actor logins, MFA, refresh tokens	90%	Refresh-token reuse detection; MFA brute-force lockout; logout endpoints
Integrations: Razorpay, iThink, Shiprocket, WhatsApp	75%	Shipping idempotency; iThink credential redaction; webhook signatures
Observability: alerts, dashboards, runbooks	40%	Cron heartbeat, financial drift alerts, top 3 incident runbooks

The 3 ship-blockers


1. **Inventory write path** — works in code review but never verified end-to-end with a real order. Sprint 1.
2. **COD UPI refunds get stuck in MANUAL_REQUIRED** — finance touches every UPI refund manually. Unsustainable past week one. Sprint 1.
3. **Refund saga has no recovery cron** — if a saga crashes mid-flight, the refund is silently lost. Sprint 1.

What we're NOT shipping in MVP-1 (and that's OK)

DEFERRED TO	WHAT	WHY IT'S OK TO DEFER
MVP-2 (Aug)	Move tokens from sessionStorage to httpOnly cookies	Coordinated FE+BE rewrite. Acceptable risk for closed beta.
MVP-2 (Aug)	Affiliate logout endpoint	Stateless 24h JWT is enough for low-volume affiliate use.
MVP-2 (Aug)	Per-line procurement tax breakdown	Admin issues tax invoice on dispatch — franchise sees it in Tax Invoices page.
MVP-3 (Sep)	Per-product SEO metadata, next/image migration	We launch via direct channels, not Google search.
MVP-3 (Sep)	Responsive breakpoints on 3 admin apps	Staff use desktop.
MVP-3 (Sep)	Per-category commission override UI	20% fallback is fine for the first seller cohort with negotiated rates.

2. The sprint plan

Timeline

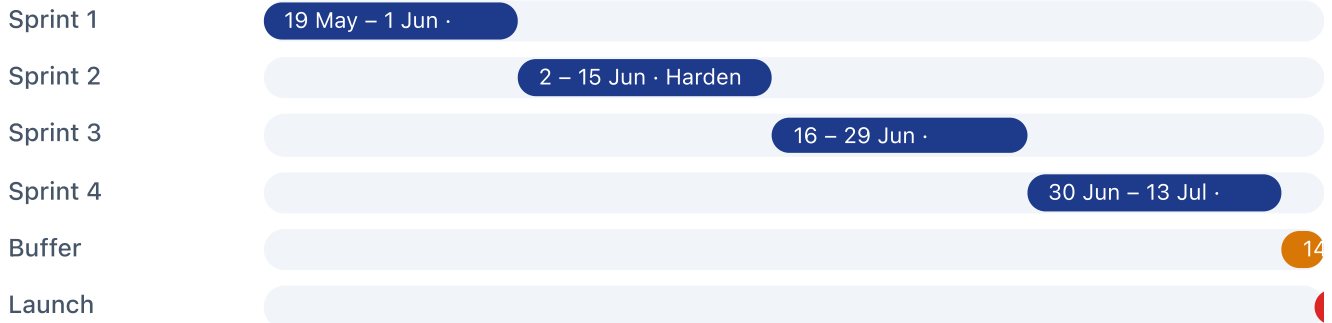

Sprint goals at a glance

SPRINT	GOAL	TOP DELIVERABLES
1. Stabilise 19 May – 1 Jun	Close every ship-blocker so we spend the rest of runway hardening, not fire-fighting.	Inventory write verified · Dispute email XSS gone · COD UPI auto-refund · Stuck-saga sweep cron · Refresh-token reuse detection · iThink credential scrubbing
2. Harden 2 – 15 Jun	Survive real load. Eliminate every race and integration-retry risk we know about.	Cart race fix · Menu reorder race fix · Shipping idempotency · iThink webhook signing · POS cross-state tax · MFA brute-force lockout · Customer/seller/franchise logout · Settlement aggregation precision
3. See 16 – 29 Jun	Make the system observable. On-call team can diagnose any incident in minutes.	Top 10 silent-failure UI fixes · Cron heartbeat dashboard · Financial drift alerts · Structured request logging · 5 golden-path E2E tests · Top 3 runbooks
4. Launch prep 30 Jun – 13 Jul	Prove it. Bug bash. Load test. Security review. Sign Go/No-Go.	Whole-team bug bash · Load test at 10× expected day-1 traffic · Security review · Production data cleanup · CS team training · Go/No-Go meeting

Key dates

DATE	WHAT
1 Jun (Fri)	Sprint 1 demo to PO + Finance + Ops
15 Jun (Mon)	Sprint 2 demo + external CA tax review
29 Jun (Mon)	Sprint 3 demo + on-call team walkthrough of runbooks
3 Jul (Fri)	Bug bash closes; P0/P1 triaged
6 Jul (Mon)	Load test results to Steering
10 Jul (Fri)	External CA signs off on tax filing readiness
12 Jul (Sat)	Go / No-Go review. Co-signed by Founder + Eng Lead.
14 Jul (Mon)	Production deploy. Smoke tests. Dry-run.
15 Jul (Wed)	LAUNCH.
1 Aug (Fri)	First GSTR-1 filing for July sales

3. Sprint detail

SPRINT 1

19 May – 1 June 2026

Stabilise

Goal: Close every ship-blocker. Inventory verified, refunds reliable, identity hardened.

WHAT WE'RE DELIVERING	DONE WHEN...	PTS
Inventory write path verified end-to-end	A real order through the storefront decrements stock + creates reservation + reverses on cancel. E2E test in CI.	3
Dispute email XSS eliminated	Admin reply text is escaped before email rendering. Same for support replies. Regression test in place.	2
COD UPI refunds auto-process	UPI refunds on COD orders flow through NEFT/IMPS automatically — no finance touch.	3
Stuck-saga sweep cron	Cron finds sagas stuck >30 min, resumes from last step, alerts on failure. Runbook published.	5
iThink credentials no longer leak to logs	Auth field redacted across all integration clients. Test asserts it.	2
Refresh-token reuse detection	Schema migration on 3 actor session tables. Stolen-token replay revokes all sessions + alerts.	5
Admin orders page error state	API failure shows error card + Retry button instead of stuck "Loading..."	3
Code hygiene	Delete 13 orphaned stub use-case files; add <code>min="0"</code> to POS price input.	2
Sprint total		25

Capacity: 28 pts planned vs ~38 pts team capacity. 10 pts buffer for slippage on the saga cron (5 pts) and the schema migration (5 pts) — both notoriously slip-prone.

Sprint risk: Schema migration on 3 actor session tables touches production-shaped data. Shadow DB validation must happen before Backend starts.

Harden money & identity

Goal: Survive real load. Kill every race and integration-retry risk we know about.

WHAT WE'RE DELIVERING	DONE WHEN...	PTS
Cart race fix	50 concurrent add-item requests produce exactly 1 CartItem row. DB-level constraint added.	3
Menu reorder race fix	Two admins reordering concurrently never produce a corrupted menu. Schema constraint backs it up.	3
Shipping create-order is idempotent	Retry with same sub-order ID returns same AWB on both iThink and Shiprocket.	3
iThink webhook signature verified	Forged tracking-update webhook returns 401 without mutating state.	2
POS cross-state tax split corrected	Tax engine uses place-of-supply from sale (customer GSTIN or franchise state) to pick CGST+SGST vs IGST. CA reviews and signs off.	2
MFA brute-force logout	5 wrong TOTP attempts invalidates the challenge token. Brute-force test fails after 5.	2
Admin password reset uses central bcrypt policy	Inline bcrypt removed; uses <code>hashPassword()</code> from policy module.	1
Server-side logout for customer / seller / franchise	3 new endpoints revoke session + clear refresh-token. Frontends wire them up.	3
Settlement aggregation drift eliminated	50-seller cycle: zero paise drift between sum-of-rows and cycle total.	3
Wallet idempotency race link	On retry-race, customer-facing tx ref matches what's in their email.	2
Discount idempotency keyed to order, not session	Cancel-and-retry checkout doesn't trip "coupon already used".	3
Sprint total		27

Capacity: 32 pts planned, 27 committed. Race-condition fixes always run long during integration testing.

Sprint risk: CA review (POS tax) may surface late-in-sprint changes. Mitigation: CA shown the engine spec in week 1, not week 2.

See — observability & tests

Goal: A stranger should be able to diagnose any incident at 3am with only the dashboard and the runbook.

WHAT WE'RE DELIVERING	DONE WHEN...	PTS
Top 10 silent-failure UI fixes	52 silent <code>.catch(() => {})</code> sites → top 10 by impact replaced with proper error UI + retry.	5
Cron heartbeat dashboard	Single screen shows every cron's last success + duration. Page-out fires if a cron goes silent.	5
Financial drift alerts	Wallet drift >₹100, refund queue stuck >24h, settlement cycle drift — all fire to Slack in staging synthetic tests.	5
Structured request logging + correlation IDs	Given an order number, on-call can pull every related backend call in seconds.	3
Webhook delivery dashboard	Last 100 webhooks per integration with success/fail/retry counts + signature outcome.	3
5 golden-path E2E tests	Playwright in CI. Tests cover customer, seller, admin, franchise, affiliate happy paths. Failing PR can't merge.	5
Top 3 operations runbooks	payment-webhook-outage, settlement-cycle-failure, stuck-refund-queue. Walked through with on-call team.	3
Cart N+1 query fix	10-item cart hits 1 batched query, not 10. Latency <200ms.	2
Sprint total		31

Sprint risk: Observability work always reveals hidden integrations. If S3.8 runs long, we ship 2 runbooks instead of 3.

Launch prep

Goal: Prove it. Bug bash, load test, security review, signed Go/No-Go.

WHAT WE'RE DELIVERING	DONE WHEN...	PTS
Bug bash week (30 Jun – 3 Jul)	Whole team walks every flow as a real user across 5 actor types. P0 fixed before week-end.	8
Load test	k6 simulates 50 req/s checkout, 200 req/s browse, 100 req/s order detail, 30 req/s payment webhook. p95 <800ms. Zero 5xx. Zero oversell.	8
Security review	Independent review of auth, payment webhooks, tax-doc download scope, OWASP Top 10 spot-check. P0/P1 findings closed.	5
Data cleanup & backfill decision	Legacy UNREGISTERED sellers: contact + 30-day grace OR soft-suspend. Stale carts TTled. Test data scrubbed.	3
Pre-deployment checklist executed	Env vars audited, backups verified, rollback tested in staging. Signed off in PR.	3
Go / No-Go meeting (12 Jul)	Every owner declares green/yellow/red. Co-signed by Founder + Eng Lead.	2
Customer support training + FAQ	2-hour session covers all 5 actor flows. Top 20 questions documented.	3
Sprint total		32

Sprint risk: Bug bash will surface 15–30 new bugs. 12 pts buffer absorbs the P0/P1 fixes. P2/P3 ship to MVP-2.

4. Launch day — Wednesday 15 July

TIME (IST)	WHAT'S HAPPENING
07:00	On-call awake. Dashboards open. Last spot-check.
08:00	Eng Lead pre-flight: env vars, backups, crons, overnight payments reconciled.
09:00	Status page live. CS team in Slack alerts channel.
09:45	Stand-up. Every team member: green / amber / red.
10:00	Flip the switch. Launch.
10:00 – 11:00	Live monitoring: API errors, payment webhooks, crons, stock-decrement-vs-order-rate sanity.
11:00	First-hour checkpoint. Eng Lead + Founder call: green / amber / red.
12:00	CS pulse-check. Marketing post on social.
15:00	Mid-day review: orders, GMV, conversion, errors.
17:00	End-of-day KPI review.
18:00	Continue / pause-for-fixes decision.
22:00	End-of-day report to Steering.

I pause ordering if any of these hit:

- API 5xx rate > 1% for 5 minutes
- Payment webhook success < 95% over 15 minutes
- Refund processor errors > 10 in 15 minutes
- Stock decrement lag > 30 seconds behind order placement
- Any CRITICAL production defect with customer impact
- Razorpay outage > 10 minutes → failover to COD-only mode

Authority to pause sits with me. Founder informed within 5 minutes.

Day 2 onwards — Hyper-care

PERIOD	COVERAGE	WHAT WE DO
Day 2 – 7	2 engineers on rotation. Daily 09:00 standup.	Triage tickets, fix P0/P1 same day, daily metric report to Steering.
Day 8 – 14	1 engineer on call. Standup 3× per week.	Ship P1 fixes. Start MVP-2 backlog grooming. First retrospective.
Day 15+	Normal cadence resumes.	MVP-2 sprint cycle begins.

Hyper-care exits when: 7 consecutive days with API 5xx < 0.5%, zero P0 incidents, support ticket / order ratio < 8%, and the first GSTR-1 filing (1 Aug) goes clean.

5. Risks, dependencies, readiness

The risks that could move the launch date

RISK	RAG	MITIGATION
Concurrent-order race causes oversell on launch	RED	Sprint 2 fix + Sprint 4 load test verifies under concurrency. If load test fails, descope to a soft-launch with rate-limited orders.
Stuck-saga cron not delivered in Sprint 1	AMBER	5 pts allocated with 10-pt sprint buffer. Mid-sprint check on 27 May; escalate if slipping.
External CA finds GST issue requiring rework	AMBER	CA shown engine spec in Sprint 1, preliminary review Sprint 3, final review 10 Jul.
Initial seller cohort under 25 → catalogue feels empty	AMBER	PO drives onboarding from Sprint 3. 5-seller minimum acceptable for soft launch.
Load test reveals deeper perf issues	AMBER	Pre-load smoke tests in Sprint 3. Cart N+1 fix in Sprint 3 buys headroom.
Razorpay outage on launch day	GREEN	COD fallback. Status page. Account manager contact ready.
Team member illness in launch week	GREEN	Pairing during Sprint 4 spreads knowledge. On-call rotation has backup.

What we need from outside the team

DEPENDENCY	OWNER	NEEDED BY
Razorpay production credentials	Founder + Razorpay AM	10 Jul
iThink production credentials	Founder + iThink AM	10 Jul
Shiprocket production credentials	Founder + Shiprocket AM	10 Jul
External CA — 2 review slots (Sprint 2 + 10 Jul)	Finance	10 Jul
SSL certificate for production domain	DevOps	10 Jul
SMTP sender domain verified	DevOps	End Sprint 3
Initial seller cohort (target 25)	Product Owner	End Sprint 4
Initial franchise cohort (target 5)	Product Owner	End Sprint 4

Open decisions (need answer)

- **POS cross-state policy:** allow walk-in customers from neighbouring states, or restrict to intra-state? — PO + Eng Lead by end Sprint 1.
- **Legacy UNREGISTERED sellers:** backfill GSTIN or soft-suspend? — PO + Finance by end Sprint 2.
- **Commission rate structure** for initial seller cohort. — PO by end Sprint 3.
- **Hosting region + DR strategy.** — DevOps + Founder by end Sprint 3.

Launch readiness — tick on 12 July

ENGINEERING	OPERATIONS	BUSINESS
☐ All MUST stories closed	☐ Env vars audited	☐ CS team trained
☐ E2E tests green in CI	☐ Backups verified (restore tested)	☐ Seller cohort onboarded
☐ Load test passes	☐ Cron heartbeat live	☐ Franchise cohort approved
☐ Security review clean	☐ Drift alerts firing	☐ Payment provider live
☐ Inventory write verified	☐ Status page live	☐ Shipping providers live
☐ Refund flows tested	☐ On-call schedule published	☐ Legal review complete
	☐ Runbooks reviewed	☐ Privacy notice published
	☐ Rollback tested	☐ Founder sign-off recorded

6. How we'll work

Team

ROLE	WHO	WHAT THEY OWN
Engineering Lead / Sprint Manager	—	Delivery, ceremonies, escalation, technical trade-offs, ~50% coding
Senior Backend Engineer	—	API, schema, integrations, payments, performance
Senior Frontend Engineer	—	8 web frontends, shared UI, customer-facing UX
QA Engineer (0.5)	—	Test automation, regression suite, sprint review
DevOps (0.25)	—	Infra, CI/CD, monitoring, deployment
Product Owner	Founder	Prioritisation, story acceptance, stakeholder comms

Cadence

CEREMONY	WHEN	WHAT WE DO
Daily stand-up	Every weekday 09:45 IST · 15 min	Yesterday / today / blockers. Done in 15 minutes or it's broken.
Sprint planning	Monday week 1, 10:00 · 2 hrs	Pick stories. Confirm acceptance. Commit.
Mid-sprint health check	Wednesday week 2, 16:00 · 30 min	Eng Lead + PO. Are we on track? Adjust scope if not.
Sprint review (demo)	Friday week 2, 14:00 · 1 hr	Demo the increment. PO accepts/rejects each story.
Retrospective	Friday week 2, 15:30 · 45 min	3 actions for next sprint. Carry them forward.
Steering review	Every alternate Friday, 11:00 · 30 min	Programme RAG + decisions. Founder + Eng Lead.

How a story moves through the sprint

It's not ready to start unless: the user story is written, acceptance criteria are testable, it's sized (1/2/3/5/8 points), dependencies are clear, and the PO has confirmed business value.

It's not done until: all acceptance criteria are met, code-reviewed by someone else, tests added, merged to `main`, deployed to staging, QA signed off, PO accepted, and no new CRITICAL/HIGH defects opened.

How I'll report to Steering each week

SECTION	CONTENT
Programme RAG	Green / Amber / Red — one line.
Sprint progress	Stories committed / delivered / carrying over.
Wins	3 bullets — what shipped that matters.
Top risks	3 risks + what I'm doing about each.
Decisions needed	Concrete asks with deadline.
Next week focus	3 bullets.

How I classify defects

SEVERITY	DEFINITION	MUST FIX WITHIN
CRITICAL	Money loss, oversell, security breach, compliance failure, customer can't transact.	24 hours
HIGH	Core flow degraded but workaround exists.	Same sprint
MEDIUM	UX issue, no business impact.	Defer to next sprint OK
LOW	Polish, cleanup, performance.	MVP-2 backlog
